

Dianne M. Triplett

July 26, 2023

VIA ELECTRONIC FILING

Adam J. Teitzman, Commission Clerk Florida Public Service Commission 2540 Shumard Oak Boulevard Tallahassee, Florida 32399-0850

Re: Petition by Duke Energy Florida, LLC, to Approve Transaction with Accelerated Decommissioning Partners, LLC, for Accelerated Decommissioning Services at the CR3 Facility, etc.

Docket No. 20190140-EI

Dear Mr. Teitzman:

Enclosed for filing on behalf of Duke Energy Florida, LLC ("DEF"), please find the Decommissioning Quarterly Report received from Accelerated Decommissioning Partners (ADP) on July 12, 2023 for the quarter ending March 2023. Order No. PSC-2020-0289-FOF-EI, dated August 27, 2020, issued in the above-referenced docket, provides that "2. The information responsive to items identified in the DSA [Decommission Services Agreement], Attachment 9, Section B through E should be provided to the Commission within two weeks of DEF's receipt of this information from ADP."

Thank you for your assistance in this matter. Please feel free to call me at (727) 820-4692 should you have any questions concerning this filing.

Sincerely,

/s/ Dianne M. Triplett

Dianne M. Triplett

DMT/mw Enclosure

299 First Avenue North (33701) • Post Office Box 14042 (33733) • St. Petersburg, Florida Phone: 727.820.4692 • Fax: 727.820.5041 • Email: dianne.triplett@duke-energy.com

CERTIFICATE OF SERVICE

I HEREBY CERTIFY that a true and correct copy of the foregoing has been furnished via electronic mail to the following this 26th day of July, 2023.

/s/ Dianne M. Triplett
Attorney

Suzanne Brownless
Florida Public Service Commission
2540 Shumard Oak Blvd.
Tallahassee, FL 32399-0850
sbrownle@psc.state.fl.us

Jon C. Moyle, Jr. / Karen A. Putnal Moyle Law Firm, P.A. 118 North Gadsden Street Tallahassee, FL 32301 jmoyle@moylelaw.com kputnal@moylelaw.com mqualls@moylelaw.com Charles J. Rehwinkel
Office of Public Counsel
c/o The Florida Legislature
111 West Madison Street, Room 812
Tallahassee, FL 32399
rehwinkel.charles@leg.state.fl.us

James W. Brew / Laura Wynn Baker Stone Mattheis Xenopoulos & Brew, PC 1025 Thomas Jefferson St., N.W. Suite 800 West Washington, DC 20007-5201 jbrew@smxblaw.com lwb@smxblaw.com





Billy E. Reid, Decommissioning Program Manager c.865.384.6789

BReid@NorthStar.com

ADP23-0022

July 12, 2023

Gene Flavors (via electronic mail)
DEF General Manager
Site Administration Building
Crystal River Energy Complex (CREC)

Subject: Materials for Quarterly Meeting

Dear Mr. Flavors,

In accordance with the Decommissioning Services Agreement (DSA) section 6.12.1 and Attachment 9, attached you will find the materials prepared by ADP CR3, LLC (ADP) for the upcoming quarterly meeting scheduled for July 25, 2023. Please note that the schedule included in the attached also satisfies the requirements for the quarterly schedule update stipulated at section 6.7 of the DSA.

Should you have any questions or comments, contact me at your convenience at either bereid@northstar.com or 865-384-6789.

Sincerely,

Billy E. Reid

Decommissioning Program Manager

Cc: Luke Self (ADP / NS)

Nelson Langub (ADP / NS) David Pearson (ADP / NS) James Seals (ADP / Orano)



Decommissioning Quarterly Report

for quarter ending

June 2023

Contents1.0EXECUTIVE SUMMARY32.0SUMMARY OF REGULATORY EVENTS AND REPORTS33.0PAY ITEM DISPUTE SUMMARY44.0ADP CR3 NON-COMPLIANCE ITEMS45.0CONCERNS NEEDING MANAGEMENT ATTENTION46.0SUBMITTED AND PENDING REGULATORY SUBMITTALS5

7.0

1.0 EXECUTIVE SUMMARY

This is the ADP CR3 quarterly report on the decommissioning of the Crystal River Unit 3 nuclear plant in accordance with the requirements of the First Amendment to the Decommissioning Services Agreement (DSA), Attachment 9, *Reporting and Notification Requirements*, reflecting the quarter from April 1, through June 30, 2023.

Q4 Safety and Environmental Performance

| Injury/Illness Summary | 2nd Quarter 2023 | YTD 2023 | PTD 2023 |
|---------------------------|---------------------|----------|----------|
| Project Hours | 114,946 | 223,720 | 922,447 |
| First Aid Cases | 2 | 2 | 15 |
| Recordable Cases | 0 | 1 | 1 |
| Lost Workday Cases | 0 | 0 | 0 |

First Aid Cases

- 04/03/2023 Employee was moving a piece of reactor mirror insulation when his hand encountered a sharp edge of metal insulation. The sharp edge cut through the employee's personnel protective outer glove (rubber) and cotton liner resulting in a laceration to the right ring finger. The employee was trying to get his leather outer gloves as defined in the Job Hazard Analysis.
- 06/20/2023 Employee was pushing a cart, transporting office materials when her arm contacted a structural column, causing a small abrasion to her left arm.
- ALARA Actual exposure to date = 47852 mrem vs budget 70754 mrem
- Personnel Contamination = 0
- Heat Stress = 0

This quarter commenced with the continuing work of draining the Reactor Cavity and preparations for Reactor Vessel Segmentation to include nozzle separations, insulation removal and grout work. Drain down completed in April and preparations for reactor segmentation is completed in June with reactor segmentation started in June. Significant progress continued in the Turbine building to allow for the building to be free released and turned over for Structural demo in July. Completed necessary facility mods to allow for interior structural demo to start in the Auxiliary Building this month. Other miscellaneous yard structures completed this quarter including Fan Building with Fans and CAS 1. Planning and preparations for other sequences of work continued this quarter. No used nuclear fuel related violations, environmental non-compliance, or significant industrial safety events occurred or were reported.

2.0 SUMMARY OF REGULATORY EVENTS AND REPORTS

Reportable events to Governmental Authority (e.g., NRC, OSHA, FDEP, EPA):

NONE

2. Receipt of any correspondence from any Governmental Authority of violation or finding: NONE

3. Any breach of debt covenants, default acceleration, insolvency, reorganization, bankruptcy or liquidation of NorthStar Group Services, Inc., and/or proposed organizational changes in equity ownership of NorthStar Group Holdings, LLC or ORANO SA:

NONE

4. Events that require Duke Energy Florida (DEF) to make a report to ANI:

NONE

5. Events that require Duke Energy Florida (DEF) to make a report to NEIL:

NONE

3.0 PAY ITEM DISPUTE SUMMARY

There are no pay items in dispute. DEF has communicated that the quality of the documentation of Pay Item completion has been very good, with progress of all Pay Item being validated.

4.0 ADP CR3 NON-COMPLIANCE ITEMS

There have been no non-compliance items this quarter.

5.0 CONCERNS NEEDING MANAGEMENT ATTENTION

No concerns needing management attention currently.

6.0 SUBMITTED AND PENDING REGULATORY SUBMITTALS

NRC Letter Log and Submittal Register


| NUMBER | DATE | FROM ORG | FROM PERSON | SUBJECT | NRC ACCESSION # |
|-----------|-----------|----------|----------------|---|--|
| N/A | 1/23/2023 | CR3 | White | DEF-Annual FFD Electronic Submittal (Electronic Only Submittal -No letter sent - 1 Month of data, final submission) | ML23023A250 |
| 3F0123-01 | 1/26/2023 | CR3 | Dixon | Crystal River Unit 3 – Proof of Financial Protection | ML23026A004 |
| 3F0323-01 | 3/2/2023 | CR3 | Dixon | Crystal River Unit 3 - Onsite Property Insurance Coverage | ML23061A011 |
| 3F0323-02 | 3/29/2023 | CR3 | State | Annual Decommissioning and Irradiated Fuel Management Financial Status Report | ML23088A387 |
| 3F0323-03 | 3/31/2023 | CR3 | State | CR3 Decommissioning Funding Plan for Independent Spent Fuel Storage Installation | ML23090A235 |
| 3F0423-01 | 4/4/2023 | CR3 | Dixon | Crystal River 3 – 2022 Individual Monitoring NRC Form 5 Report | ML23094A079 |
| 3F0423-02 | 4/18/2023 | CR3 | Dixon | Crystal River 3 - 2022 Annual Radioactive Effluent Release Report | ML23108A264 |
| 3F0423-03 | 4/18/2023 | CR3 | Dixon | Crystal River 3 - 2022 Annual Radiological Environmental Operating Report | ML23108A266 |
| 3F0523-01 | 5/24/2023 | CR3 | Adix | Crystal River 3 – Annual Financial Report and Certified Financial Statement | ML23144A258 |
| 3F0623-01 | 6/1/2023 | CR3 | Reid | Late Received Radiological Shipment | ML23152A263 |
| 3F0623-02 | 6/9/2023 | CR3 | Reid | LTP Resubmittal | ML23160A296 ML23160A297 ML23160A298 ML23160A299 |

| 2023 Crystal River 3 – NRC Submittals | | | | | |
|--|--|--|--|--|--|
| Submittal | Submittal to be Signed | Comments | | | |
| License Termination Plan License Amendment | December 31, 2022 | 10CFR 50.82(a)(9) | | | |
| - Soil Contour on Settling Ponds | | Awaiting confirmation notice that confirmatory samples not required | | | |
| Proof of Financial Protection, Financial Liability Policy Renewal (ANI) | January 31, 2023 | 10 CFR 140.15, 140.11(a)(4) Exempted, 10 CFR 140.17(b) | | | |
| Annual Report for Drug and Alcohol Tests (Electronic Submittal by Security) | March 1, 2023 | 10 CFR 26.417(b)(2) and 26.717. (LIMITED REPORT FOR 1 MONTH OF 2022) NRC Form 891, Annual Reporting Form for Drug and Alcohol Tests | | | |
| ISFSI Triennial | March 31, 2023 | 10 CFR 72 30(c) | | | |
| Annual Decommissioning and Irradiated Fuel Management Financial Status Report | March 31, 2023 | 10 CFR 50.82(a)(8)(v), (vi) and (vii) and 10 CFR 50.75(f)(1) and (2) | | | |
| Copy of Material Balance Report and Physical Inventory Listing Report (12 month frequency requirement from last submittal) | March 31, 2023 | 10 CFR 74.13(a) and 10 CFR 74.15, 10 CFR 70.55, 10 CFR 72.76, 10 CFR 72.78, (Within 60 days following the start of the annual physical inventory of special nuclear material and/or source material) | | | |
| Onsite Property Insurance Coverage (NEIL) | April 1, 2023 | 10 CFR 50.54(w)(3) | | | |
| Radiation Exposure Report To Employees (RPCM initiates) | April 30, 2023 | 10 CFR 19.13(b) and 10 CFR 20.2206 | | | |
| Annual Radioactive Effluent Release Report and a copy of the ODCM | May 1, 2023 | Submit report per 10 CFR 50.36a(a)(2) and ODCM; 10 CFR 72.44(d)(3) | | | |
| Annual Radioactive Radiological Environmental Operating Report | May 15, 2023 | 10 CFR 72.44(d)(3); Submit report per ODCM | | | |
| Annual Copy of Corporate Financial Report See 10 CFR 140.15 (a) | Annually (within 30 days of issuance of annual report) | 10 CFR 50.71(b) 10 CFR 72.80(b) | | | |
| Crystal River Unit 3 – Reporting Related to the National Pollutant Discharge Elimination System (NPDES) Permit ID# FL0A00004-001-IW1S | As needed | CP-500 | | | |
| Crystal River 3 – Report of Investigation Pursuant to 10 CFR 20, Appendix G. | As needed | 10 CFR 20, Appendix G, as exempted | | | |
| Shipment Notification of Irradiated Fuel or Wastes Across States or Tribal Reservations | As needed | 10 CFR 71.97 Postmarked at least 7 days before shipment or 4 days otherwise | | | |

| | Submittals | NRC Accession/ TAC Number | NRC Approval Requested | Next Expected Action | Comments |
|--|--|--|---------------------------|--------------------------|---------------------|
| License Termination Plan License Amendment | | ML22355A441 | | | |
| - | Request for Supplemental Inform. for Acceptance Review | ML23103A189 | | | Response due June 1 |
| | Supplemental Information Submitted June 9 | ML23160A296 ML23160A297 ML23160A298 ML23160A299 | | NRC Acceptance Review | |

Environmental

| Number | Date | From Org | From Person | Subject | Submitted To |
|-------------------|-------------------|-----------------|-----------------------|--|-------------------------|
| ite Investigation | n/Remediation | | | | * |
| | 2-Feb-23 | ADP CR3 | Nadia Glucksberg | Revised Supplemental Report | FDEP |
| | 13-Feb-23 | ADP CR3 | Nadia Glucksberg | Evaluation of Subgrade Coated Concrete | FDEP |
| | 13-Feb-23 | ADP CR3 | Nadia Glucksberg | Technical Meeting - Coatings on Basement Strucutres (for new FDEP Project Manager) | FDEP |
| | 2/6 - 2/16/23 | Haley & Aldrich | Miles van Noordennen | AOC2 UST - Fuel Oil UST - Investigations Completed | ADP CR3 |
| | 3/24/2023 | ADP CR3 | Nadia Glucksberg | Site Visit re: Supplemental Investigation Report and Background Evaluation | FDEP |
| | 1-Apr-23 | Haley & Aldrich | Miles van Noordennen | Piping Evaluation Draft | ADP CR3 |
| | 9-Jun-23 | Haley & Aldrich | Elida Danaher | LTP Chapter 2 Revision (in progress) | ADP CR3 |
| | 8-May-23 | FDEP | John Sego | Evaluation of Coatings and Subgrade Structures - Review/Approval | ADP CR3 |
| ermits | | | | | |
| | ongoing | Haley & Aldrich | Elida Danaher | Monthly DMRs per NPDES Permit | FDEP |
| | 27-Feb-23 | Haley & Aldrich | Elida Danaher | Tier II Submittal | FDEP |
| | Mar-23 | Haley & Aldrich | Elida Danaher | Updated Duly Authorized Agent for NPDES permit | FDEP |
| | ongoing | Haley & Aldrich | Nadia Glucksberg | Attended monthly and quaterly updates with DEF | NA |
| | Apr-23 | Haley & Aldrich | Nadia Glucksberg | Haz Waste Inspection Response Letter | FDEP |
| | 5/23/2023 | FDEP | Molly Enck | Haz Waste Inspection Approval | ADP CR3 |
| | 6/23/2023 | FDEP | Steven Tafuni | MSGP Inspection Approval | ADP CR3 |
| | expected 6/30/23 | Haley & Aldrich | Nadia Glucksberg | MSGP Minor Modification | FDEP |
| ermitting Suppo | ort | | | | |
| | confirmed 2/23/23 | ADP CR3 | Elida Danaher | Update to Duly Authorized Agent with FDEP (mutiple communications) | FDEP |
| | 2/23/2022 | ADP CR3 | Elida Danaher | Tier II Inspection & Report | E-plan reporting system |
| | 3/6/2023 | Haley & Aldrich | Elida Danaher | Haz Waste Inspection | FDEP |
| | 3/14-3/15/23 | Haley & Aldrich | Miles VanNoordennen | Waste Characterization | ADP CR3 |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | | | | |
| | | H&A | Flide Develop & Miles | Weekly Support for Permitting | ADP CR3 |
| | ongoing | | | | |

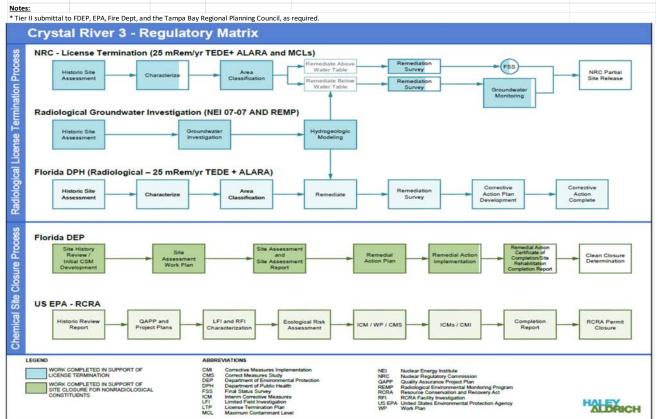

7.0 COMPLETED AND NEAR-TERM SCHEDULE MILESTONES

| | PAY ITEM/MILESTONE | PLANNED COMPLETE | STATUS |
|---------|---|---------------------|-------------------|
| 3.1.1.1 | Planning & Site Preparation | | 100% |
| 3.1.1.1 | Utilities Reactivation | | Complete |
| 3.1.1.2 | Planning & Site Preparation | | 100% |
| 3.1.1.2 | Containment Access, Waste Handling Areas | | Complete |
| 3.1.2 | Planning & Site Preparation | | 100% |
| 3.1.2 | Site Characterization | | Complete |
| | Planning & Site Preparation | | 1000/ |
| 3.1.3.1 | LCR and RV/RVI Planning and Engineering | | 100% Complete |
| | General transition Planning/Engineering | | complete |
| | Planning & Site Preparation | | |
| 3.1.3.2 | LCR and RV/RVI Planning and Engineering | | 100% Complete |
| | Site/Plant infrastructure Planning and Engineering | | Complete |
| | Planning & Site Preparation | | |
| 3.1.3.3 | LCR and RV/RVI Planning and Engineering | | 100 % Complete |
| | RVI Planning and Engineering | | Complete |
| | Planning & Site Preparation | | |
| 3.1.3.4 | LCR and RV/RVI Planning and Engineering | 10/10/2023 | 77% Complete |
| | RV Planning and Engineering | | |
| | Planning & Site Preparation | | |
| 3.1.3.5 | LCR and RV/RVI Planning and Engineering | | 100% Complete |
| | LCR Planning and Engineering | | Complete |
| | Planning & Site Preparation | | |
| 3.1.4.1 | Balance of Plant D&D Planning | | 100% |
| | Temporary Utilities, Site Preparation Planning | | Complete |
| | Planning & Site Preparation | | |
| 3.1.4.2 | Balance of Plant D&D Planning | | 100% |
| | Turbine, Condenser, Steam Generator Removal Planning | | Complete |
| | Planning & Site Preparation | | |
| 3.1.4.3 | Balance of Plant D&D Planning | | 100% |
| | Systems Removal and Decon Work Planning | | Complete |
| | Planning & Site Preparation | | |
| 3.1.4.4 | Balance of Plant D&D Planning | 12/31/2023 | 49% |
| | Demolition Work Planning | | Complete |
| | Large Component Removal | | 100% |
| 4.A.1.1 | Reactor Internals Segmentation | | Complete |
| 4 4 6 5 | Reactor Internals Mobilization, Setup & Commissioning | | - |
| 4.A.1.2 | Large Component Removal | | 100% |

| | PAY ITEM/MILESTONE | PLANNED COMPLETE | STATUS |
|---------|---|---------------------|------------------|
| | Reactor Internals Segmentation Reactor Internals Segmentation (Plenum Assembly) | | Complete |
| 4.A.1.3 | Large Component Removal Reactor Internals Segmentation Reactor Internals Segmentation (Core Support Assembly/Remaining) | | 100% Complete |
| 4.A.1.4 | Large Component Removal Reactor Internals Segmentation Reactor Internals Waste Packaging, Transportation and Disposal | 12/31/2023 | 20% Complete |
| 4.A.2.1 | Large Component Removal Reactor Vessel Segmentation Reactor Vessel Mobilization | | 100% Complete |
| 4.A.2.2 | Large Component Removal Reactor Vessel Segmentation Reactor Vessel Segmentation | 9/20/2023 | 10% Complete |
| 4.A.3 | Large Component Removal Reactor Vessel Segmentation Reactor CRDMs, ICIs, Services Structure | | 100% Complete |
| 4.A.4.1 | Large Component Removal Reactor Coolant System Reactor Coolant Piping | | 100% Complete |
| 4.A.4.2 | Large Component Removal Reactor Coolant System Reactor Coolant System Pumps and Motors | | 100% Complete |
| 4.A.5 | Large Component Removal Reactor Coolant System Pressurizer and Relief Tank | | 100% Complete |
| 4.A.6.5 | Large Component Removal Steam Generators Steam Generator Package, Transportation and Disposal | | 100% Complete |
| 4.A.7.1 | Large Component Removal Main Turbine/Generator/Condensers Turbine and Generator Removal | | 100% Complete |
| 4.A.7.1 | Large Component Removal Condenser Removal | | 100% Complete |
| 4.B.1.2 | Site Decontamination Remove Plant Systems Auxiliary Building elev 95' | 12/16/2023 | 76% Complete |
| 4.B.1.3 | Site Decontamination Remove Plant Systems Auxiliary Building elev 119' | 01/02/2024 | 72% Complete |
| 4.B.1.4 | Site Decontamination Remove Plant Systems Intermediate Building | | 100% Complete |
| 4.B.1.5 | Site Decontamination | | 100% |


| | PAY ITEM/MILESTONE | PLANNED COMPLETE | STATUS |
|---------|---|---------------------|------------------|
| | Remove Plant Systems Turbine Building | | Complete |
| 4.B.4 | Site Decontamination Decontaminate Buildings License Termination Planning | | 100% Complete |
| 4.B.5.1 | Site Decontamination Decontaminate Buildings West Settling Pond Remediation | | 100% Complete |
| 4.B.5.3 | Site Decontamination Decontaminate Buildings Transfer Canal Sand Removal | | 100% Complete |
| 5.1.1 | Site Restoration Demolish Turbine Building | 12/15/2023 | 0% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures Emergency Feed Water Building | | 100% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures Diesel Generator Building | | 100% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures Alternate AC Diesel Generator Bldg Demo | | 100% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures Fire Pump House Building | | 100% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures RB Maintenance Bldg Demo | | 100% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures RX Vessel Closure Head Storage Bldg Demo | | 100% Complete |
| 5.1.2 | Site Restoration Demolish Miscellaneous Site Structures Hot and Cold Shopt Bldg Demo | 8/31/2023 | 0% Complete |
| 5.2.1 | Site Restoration Firing Range Closure | | 100% Complete |

Notes:

Progress Photos

Large Component Removal Work

Fuel Transfer Canal Drain Down

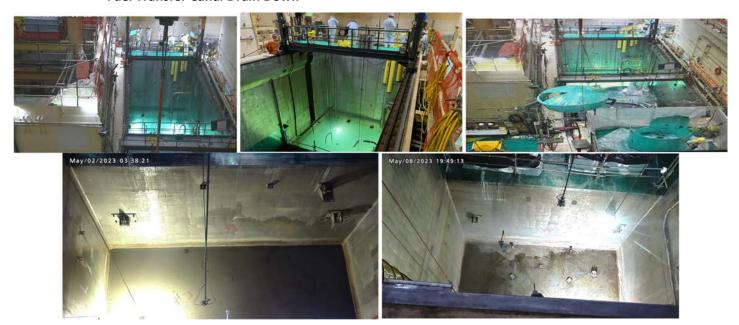

Reactor Vessel Internals Secondary Waste Shpment



Reactor Vessel Working Platform



Arrival of Top Package







Mobilization of Crane and Rigging Equipment







Condenser Removal



<u>Site Decon – Remove Plant Systems</u>

Auxiliary Building Systems Removal







Control Complex Systems Removal





Turbine Building Systems Removal









<u>Site Restoration – Misc Building Demolition</u>

Fan Room








CAS 1 Demolition



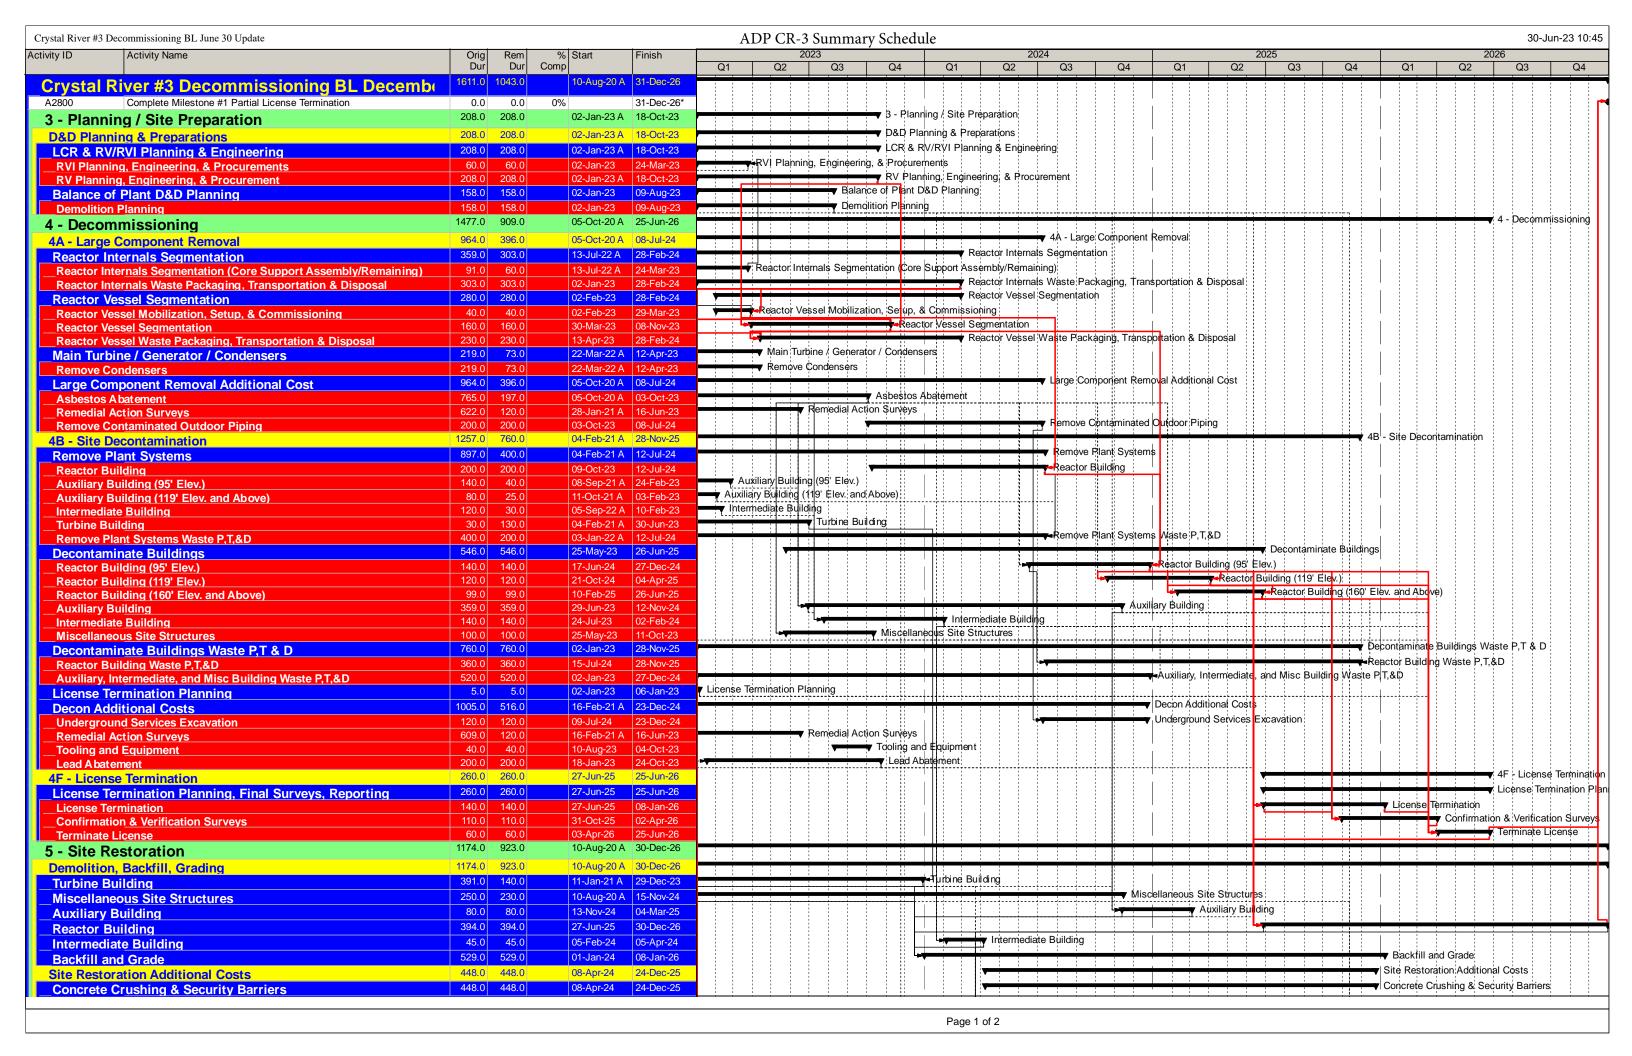

| Crystal River #3 Decommissioning BL June 30 Update | | 455 05 0 0 Ochodula | | 30-Jun-23 10:45 |
|--|--------------------------------------|--|-------------------|---------------------------------|
| Activity ID Activity Name | Orig Rem % Start Finish Dur Dur Comp | ADP CR-3 Summary Schedule | 2024 2025 | 2026 |
| Croncrete Crushing | Dur Dur Comp | Q1 Q2 Q3 Q4 Q1 | Q2 Q3 Q4 Q1 Q2 Q3 | Q4 Q1 Q2 Q3 Q4 |
| Security VBS | 19.0 19.0 28-Nov-25 24-Dec-25 | CR3 D&D Project - GTCC Management | | Croncrete Crushing Security VBS |
| CR3 D&D Project - GTCC Management | 34.0 34.0 10-Jan-23 00-War-23 | To the second se | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | Page 2 of | 2 | |
| | | | | |

