



Dianne M. Triplett
DEPUTY GENERAL COUNSEL

October 19, 2023

VIA ELECTRONIC FILING

Adam J. Teitzman, Commission Clerk
Florida Public Service Commission
2540 Shumard Oak Boulevard
Tallahassee, Florida 32399-0850

Re: *Petition by Duke Energy Florida, LLC, to Approve Transaction with Accelerated Decommissioning Partners, LLC, for Accelerated Decommissioning Services at the CR3 Facility, etc.*
Docket No. 20190140-EI

Dear Mr. Teitzman:

Enclosed for filing on behalf of Duke Energy Florida, LLC (“DEF”), please find the Decommissioning Quarterly Report received from Accelerated Decommissioning Partners (ADP) on October 11, 2023 for the quarter ending September 2023. Order No. PSC-2020-0289-FOF-EI, dated August 27, 2020, issued in the above-referenced docket, provides that “2. The information responsive to items identified in the DSA [Decommission Services Agreement], Attachment 9, Section B through E should be provided to the Commission within two weeks of DEF’s receipt of this information from ADP.”

Thank you for your assistance in this matter. Please feel free to call me at (727) 820-4692 should you have any questions concerning this filing.

Sincerely,

/s/ Dianne M. Triplett

Dianne M. Triplett

DMT/mw
Enclosure

CERTIFICATE OF SERVICE

I HEREBY CERTIFY that a true and correct copy of the foregoing has been furnished via electronic mail to the following this 19th day of October, 2023.

/s/ Dianne M. Triplett

Attorney

<p>Suzanne Brownless Florida Public Service Commission 2540 Shumard Oak Blvd. Tallahassee, FL 32399-0850 sbrownle@psc.state.fl.us</p> <p>Jon C. Moyle, Jr. / Karen A. Putnal Moyle Law Firm, P.A. 118 North Gadsden Street Tallahassee, FL 32301 jmoyle@moylelaw.com kputnal@moylelaw.com mqualls@moylelaw.com</p>	<p>Charles J. Rehwinkel Office of Public Counsel c/o The Florida Legislature 111 West Madison Street, Room 812 Tallahassee, FL 32399 rehwinkel.charles@leg.state.fl.us</p> <p>James W. Brew / Laura Wynn Baker Stone Mattheis Xenopoulos & Brew, PC 1025 Thomas Jefferson St., N.W. Suite 800 West Washington, DC 20007-5201 jbrew@smxblaw.com lwb@smxblaw.com</p>
---	---



Billy E. Reid, Decommissioning Program Manager

c.865.384.6789

BReid@NorthStar.com

ADP23-0022

October 11, 2023

Gene Flavors (via electronic mail)
DEF General Manager
Site Administration Building
Crystal River Energy Complex (CREC)

Subject: Materials for Quarterly Meeting

Dear Mr. Flavors,

In accordance with the Decommissioning Services Agreement (DSA) section 6.12.1 and Attachment 9, attached you will find the materials prepared by ADP CR3, LLC (ADP) for the upcoming quarterly meeting scheduled for October 25, 2023. Please note that the schedule included in the attached also satisfies the requirements for the quarterly schedule update stipulated at section 6.7 of the DSA.

Should you have any questions or comments, contact me at your convenience at either bereid@northstar.com or 865-384-6789.

Sincerely,

A handwritten signature in blue ink that reads "Billy E. Reid".

Billy E. Reid
Decommissioning Program Manager

Cc: Luke Self (ADP / NS)
Nelson Langub (ADP / NS)
David Pearson (ADP / NS)
James Seals (ADP / Orano)



Decommissioning Quarterly Report

for quarter ending

September 2023

Contents

1.0	EXECUTIVE SUMMARY	3
2.0	SUMMARY OF REGULATORY EVENTS AND REPORTS	3
3.0	PAY ITEM DISPUTE SUMMARY	4
4.0	ADP CR3 NON-COMPLIANCE ITEMS.....	4
5.0	CONCERNS NEEDING MANAGEMENT ATTENTION	4
6.0	SUBMITTED AND PENDING REGULATORY SUBMITTALS.....	5
7.0	COMPLETED AND NEAR-TERM SCHEDULE MILESTONES.....	7

1.0 EXECUTIVE SUMMARY

This is the ADP CR3 quarterly report on the decommissioning of the Crystal River Unit 3 nuclear plant in accordance with the requirements of the First Amendment to the Decommissioning Services Agreement (DSA), Attachment 9, *Reporting and Notification Requirements*, reflecting the quarter from July 1, through September 30, 2023.

Q4 Safety and Environmental Performance

Injury/Illness Summary	3rd Quarter 2023	YTD 2023	PTD 2023
Project Hours	97,362	321,280	1,020,007
First Aid Cases	1	3	16
Recordable Cases	0	1	1
Lost Workday Cases	0	0	0

- First Aid Case
 - **8/9/2023** Employee was on the 162' elevation of the Auxiliary Building, working with the crew mechanically removing the concrete floor. Wood planking was installed prior to beginning the work. Under the concrete flooring, screws were used to secure the wood planking to the corrugated metal. The crew was bending the screws over as they removed the wood planking and inadvertently missed one. The employee stepped on the screw causing a minor puncture to the bottom of his foot.
- ALARA Actual exposure to date = 58214 mrem vs budget 65346 mrem
- Personnel Contamination = 1 Level 1 PCE, Worker rubbed shirt collar on contaminated rope at equipment hatch
 - NRC RP Inspections identified no discrepancies.
- Heat Stress = 0

This quarter commenced with the continuing work of Reactor Vessel Segmentation to remove top and middle sections of the reactor and placing them into their packaging, insulation removal and grout work. Significant progress continued in the Turbine building to allow for the building to be free released and turned over for Structural demo in July. Interior demolition of both the Auxiliary and Turbine building progressed this month. Other miscellaneous yard structures completed this quarter including Hot and Cold shops. Planning and preparations for other sequences of work continued this quarter. No used nuclear fuel related violations, environmental non-compliance, or significant industrial safety events occurred or were reported.

2.0 SUMMARY OF REGULATORY EVENTS AND REPORTS

1. Reportable events to Governmental Authority (e.g., NRC, OSHA, FDEP, EPA):

NONE

2. Receipt of any correspondence from any Governmental Authority of violation or finding:
NONE
3. Any breach of debt covenants, default acceleration, insolvency, reorganization, bankruptcy or liquidation of NorthStar Group Services, Inc., and/or proposed organizational changes in equity ownership of NorthStar Group Holdings, LLC or ORANO SA:
NONE
4. Events that require Duke Energy Florida (DEF) to make a report to ANI:
NONE
5. Events that require Duke Energy Florida (DEF) to make a report to NEIL:
NONE

3.0 PAY ITEM DISPUTE SUMMARY

There are no pay items in dispute. DEF has communicated that the quality of the documentation of Pay Item completion has been very good, with progress of all Pay Item being validated.

4.0 ADP CR3 NON-COMPLIANCE ITEMS

There have been no non-compliance items this quarter.

5.0 CONCERNS NEEDING MANAGEMENT ATTENTION

No concerns needing management attention currently.

ADP CR3 Decommissioning Quarterly Report
3Q-2023

6.0 SUBMITTED AND PENDING REGULATORY SUBMITTALS

NRC Letter Log and Submittal Register

NUMBER	DATE	FROM ORG	FROM PERSON	SUBJECT	NRC ACCESSION #
N/A	1/23/2023	CR3	White	DEF-Annual FFD Electronic Submittal (Electronic Only Submittal -No letter sent - 1 Month of data, final submission)	ML23023A250
3F0123-01	1/26/2023	CR3	Dixon	Crystal River Unit 3 – Proof of Financial Protection	ML23026A004
3F0323-01	3/2/2023	CR3	Dixon	Crystal River Unit 3 - Onsite Property Insurance Coverage	ML23061A011
3F0323-02	3/29/2023	CR3	State	Annual Decommissioning and Irradiated Fuel Management Financial Status Report	ML23088A387
3F0323-03	3/31/2023	CR3	State	CR3 Decommissioning Funding Plan for Independent Spent Fuel Storage Installation	ML23090A235
3F0423-01	4/4/2023	CR3	Dixon	Crystal River 3 – 2022 Individual Monitoring NRC Form 5 Report	ML23094A079
3F0423-02	4/18/2023	CR3	Dixon	Crystal River 3 - 2022 Annual Radioactive Effluent Release Report	ML23108A264
3F0423-03	4/18/2023	CR3	Dixon	Crystal River 3 - 2022 Annual Radiological Environmental Operating Report	ML23108A266
3F0523-01	5/24/2023	CR3	Adix	Crystal River 3 – Annual Financial Report and Certified Financial Statement	ML23144A258
3F0623-01	6/1/2023	CR3	Reid	Late Received Radiological Shipment	ML23152A263
3F0623-02	6/9/2023	CR3	Reid	LTP Resubmittal	ML23160A296 ML23160A297 ML23160A298 ML23160A299


2023 Crystal River 3 – NRC Submittals		
Submittal	Submittal to be Signed	Comments
License Termination Plan License Amendment	December 31, 2022	10CFR 50.82(a)(9)
- Soil Contour on Settling Ponds		Awaiting confirmation notice that confirmatory samples not required
Proof of Financial Protection, Financial Liability Policy Renewal (ANI)	January 31, 2023	10 CFR 140.15, 140.11(a)(4) Exempted, 10 CFR 140.17(b)
Annual Report for Drug and Alcohol Tests (Electronic Submittal by Security)	March 1, 2023	10 CFR 26.417(b)(2) and 26.717. (LIMITED REPORT FOR 1 MONTH OF 2022) NRC Form 891, Annual Reporting Form for Drug and Alcohol Tests
ISFSI Triennial	March 31, 2023	10 CFR 72.30(c)
Annual Decommissioning and Irradiated Fuel Management Financial Status Report	March 31, 2023	10 CFR 50.82(a)(8)(v), (vi) and (vii) and 10 CFR 50.75(f)(1) and (2)
Copy of Material Balance Report and Physical Inventory Listing Report (12 month frequency requirement from last submittal)	March 31, 2023	10 CFR 74.13(a) and 10 CFR 74.15, 10 CFR 70.55, 10 CFR 72.76, 10 CFR 72.78, (Within 90 days following the start of the annual physical inventory of special nuclear material and/or source material)
Onsite Property Insurance Coverage (NEIL)	April 1, 2023	10 CFR 50.54(w)(3)
Radiation Exposure Report To Employees (RPCM initiates)	April 30, 2023	10 CFR 19.13(b) and 10 CFR 20.2206
Annual Radioactive Effluent Release Report and a copy of the ODCM	May 1, 2023	Submit report per 10 CFR 50.36(a)(2) and ODCM; 10 CFR 72.44(d)(3)
Annual Radioactive Radiological Environmental Operating Report	May 15, 2023	10 CFR 72.44(d)(3); Submit report per ODCM
Annual Copy of Corporate Financial Report See 10 CFR 140.15 (a)	Annually (within 30 days of issuance of annual report)	10 CFR 50.71(b) 10 CFR 72.80(b)
Crystal River Unit 3 – Reporting Related to the National Pollutant Discharge Elimination System (NPDES) Permit ID# FL0A00004-001-IW1S	As needed	CP-500
Crystal River 3 – Report of Investigation Pursuant to 10 CFR 20, Appendix G.	As needed	10 CFR 20, Appendix G, as exempted
Shipment Notification of Irradiated Fuel or Wastes Across States or Tribal Reservations	As needed	10 CFR 71.97 Postmarked at least 7 days before shipment or 4 days otherwise

Submittals	NRC Accession/ TAC Number	NRC Approval Requested	Next Expected Action	Comments
License Termination Plan License Amendment	ML22355A441			
- Request for Supplemental Inform. for Acceptance Review	ML23103A189			Response due June 1
- Supplemental Information Submitted June 9	ML23160A296 ML23160A297 ML23160A298 ML23160A299		NRC Acceptance Review	

ADP CR3 Decommissioning Quarterly Report 3Q-2023

Environmental

Summary of Haley & Aldrich Submittals and Actions Q3 2023 (July through Sept)					
Number	Date	From Org	From Person	Subject	Submitted To
Site Investigation/Remediation					
	2-Feb-23	ADP CR3	Nadia Glucksberg	Revised Supplemental Report	FDEP
	13-Feb-23	ADP CR3	Nadia Glucksberg	Evaluation of Subgrade Coated Concrete	FDEP
	13-Feb-23	ADP CR3	Nadia Glucksberg	Technical Meeting - Coatings on Basement Structures (for new FDEP Project Manager)	FDEP
	2/6 - 2/16/23	Haley & Aldrich	Miles van Noordennen	AOC2 UST - Fuel Oil UST - Investigations Completed	ADP CR3
	3/24/2023	ADP CR3	Nadia Glucksberg	Site Visit re: Supplemental Investigation Report and Background Evaluation	FDEP
	1-Apr-23	Haley & Aldrich	Miles van Noordennen	Piping Evaluation Draft	ADP CR3
	9-Jun-23	Haley & Aldrich	Elida Danaher	LTP Chapter 2 Revision (in progress)	ADP CR3
	8-May-23	FDEP	John Sego	Evaluation of Coatings and Subgrade Structures - Review/Approval	ADP CR3
Permits					
	ongoing	Haley & Aldrich	Elida Danaher	Monthly DMRs per NPDES Permit	FDEP
	27-Feb-23	Haley & Aldrich	Elida Danaher	Tier II Submittal	FDEP
	Mar-23	Haley & Aldrich	Elida Danaher	Updated Duly Authorized Agent for NPDES permit	FDEP
	ongoing	Haley & Aldrich	Nadia Glucksberg	Attended monthly and quarterly updates with DEF	NA
	Apr-23	Haley & Aldrich	Nadia Glucksberg	Haz Waste Inspection Response Letter	FDEP
	5/23/2023	FDEP	Molly Enck	Haz Waste Inspection Approval	ADP CR3
	6/23/2023	FDEP	Steven Tafuni	MSGP Inspection Approval	ADP CR3
	7/11/2023	Haley & Aldrich	Nadia Glucksberg	MSGP Minor Modification Request	FDEP
	7/24/23	FDEP	Krishna Baral	MSGP Modification Approval	ADP CR3
Permitting Support					
	confirmed 2/23/23	ADP CR3	Elida Danaher	Update to Duly Authorized Agent with FDEP (mutiple communications)	FDEP
	2/23/2022	ADP CR3	Elida Danaher	Tier II Inspection & Report	E-plan reporting system*
	3/6/2023	Haley & Aldrich	Elida Danaher	Haz Waste Inspection	FDEP
	3/14-3/15/23	Haley & Aldrich	Miles VanNoordennen	Waste Characterization	ADP CR3
	8/2/23	Haley & Aldrich	Scott Underhill	Annual ERP Inspection	ADP CR3
	9/26/23	Haley & Aldrich	Nadia Glucksberg	MSGP vs NPDES White Paper	ADP CR3
	ongoing	H&A	Elida Danaher & Miles van Noordennen	Weekly Support for Permitting	ADP CR3

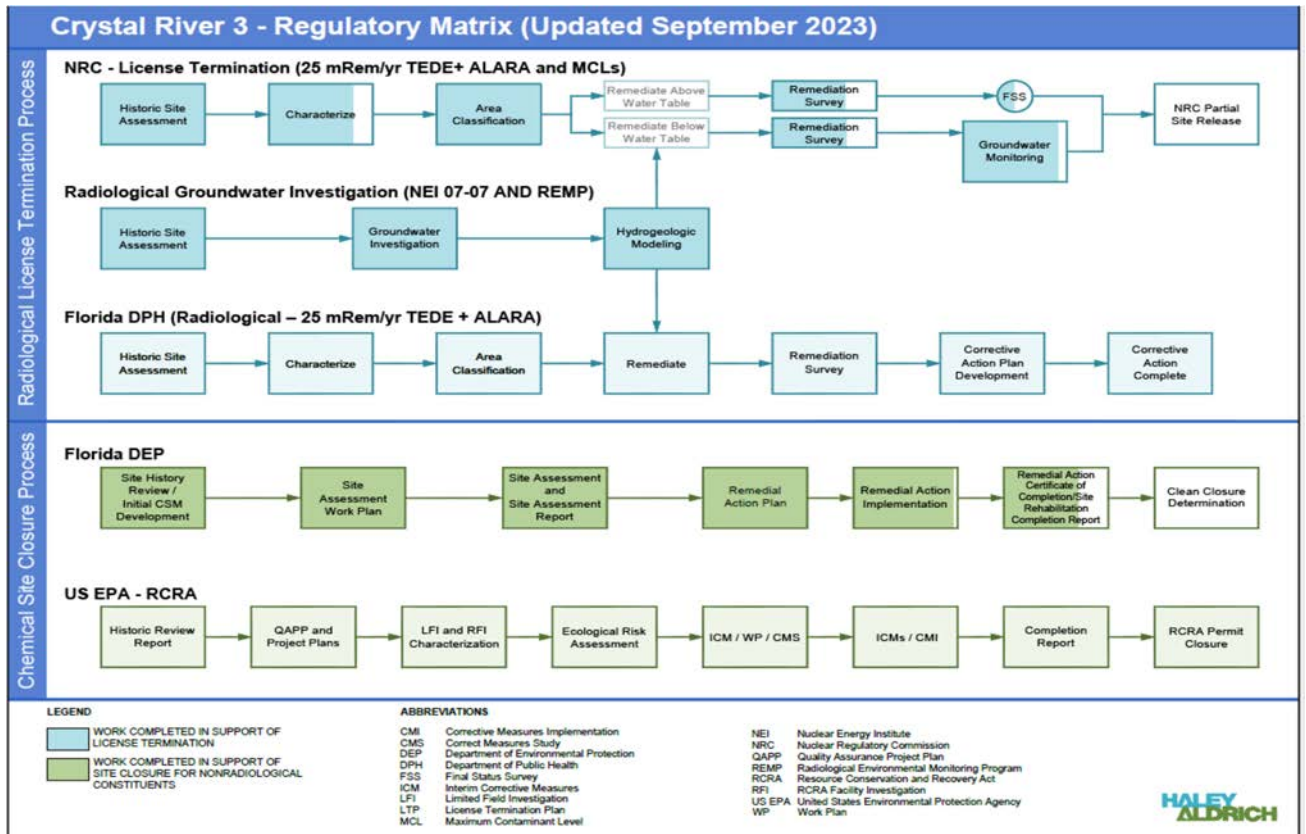

7.0 COMPLETED AND NEAR-TERM SCHEDULE MILESTONES

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
3.1.1.1	Planning & Site Preparation Utilities Reactivation		100% Complete
3.1.1.2	Planning & Site Preparation Containment Access, Waste Handling Areas		100% Complete
3.1.2	Planning & Site Preparation Site Characterization		100% Complete
3.1.3.1	Planning & Site Preparation LCR and RV/RVI Planning and Engineering General transition Planning/Engineering		100% Complete
3.1.3.2	Planning & Site Preparation LCR and RV/RVI Planning and Engineering Site/Plant infrastructure Planning and Engineering		100% Complete
3.1.3.3	Planning & Site Preparation LCR and RV/RVI Planning and Engineering RVI Planning and Engineering		100 % Complete
3.1.3.4	Planning & Site Preparation LCR and RV/RVI Planning and Engineering RV Planning and Engineering	10/20/2023	77% Complete
3.1.3.5	Planning & Site Preparation LCR and RV/RVI Planning and Engineering LCR Planning and Engineering		100% Complete
3.1.4.1	Planning & Site Preparation Balance of Plant D&D Planning Temporary Utilities, Site Preparation Planning		100% Complete
3.1.4.2	Planning & Site Preparation Balance of Plant D&D Planning Turbine, Condenser, Steam Generator Removal Planning		100% Complete
3.1.4.3	Planning & Site Preparation Balance of Plant D&D Planning Systems Removal and Decon Work Planning		100% Complete
3.1.4.4	Planning & Site Preparation Balance of Plant D&D Planning Demolition Work Planning	12/31/2023	49% Complete
4.A.1.1	Large Component Removal Reactor Internals Segmentation Reactor Internals Mobilization, Setup & Commissioning		100% Complete
4.A.1.2	Large Component Removal		100%

ADP CR3 Decommissioning Quarterly Report
3Q-2023

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
	Reactor Internals Segmentation Reactor Internals Segmentation (Plenum Assembly)		Complete
4.A.1.3	Large Component Removal Reactor Internals Segmentation Reactor Internals Segmentation (Core Support Assembly/Remaining)		100% Complete
4.A.1.4	Large Component Removal Reactor Internals Segmentation Reactor Internals Waste Packaging, Transportation and Disposal	5/31/2024	20% Complete
4.A.2.1	Large Component Removal Reactor Vessel Segmentation Reactor Vessel Mobilization		100% Complete
4.A.2.2	Large Component Removal Reactor Vessel Segmentation Reactor Vessel Segmentation	10/20/2023	10% Complete
4.A.3	Large Component Removal Reactor Vessel Segmentation Reactor CRDMs, ICIs, Services Structure		100% Complete
4.A.4.1	Large Component Removal Reactor Coolant System Reactor Coolant Piping		100% Complete
4.A.4.2	Large Component Removal Reactor Coolant System Reactor Coolant System Pumps and Motors		100% Complete
4.A.5	Large Component Removal Reactor Coolant System Pressurizer and Relief Tank		100% Complete
4.A.6.5	Large Component Removal Steam Generators Steam Generator Package, Transportation and Disposal		100% Complete
4.A.7.1	Large Component Removal Main Turbine/Generator/Condensers Turbine and Generator Removal		100% Complete
4.A.7.1	Large Component Removal Condenser Removal		100% Complete
4.B.1.1	Site Decontamination Remove Plant Systems Reactor Building	6/1/2024	5% Complete
4.B.1.2	Site Decontamination Remove Plant Systems Auxiliary Building elev 95'	12/16/2023	83% Complete
4.B.1.3	Site Decontamination Remove Plant Systems Auxiliary Building elev 119'	01/02/2024	81% Complete
4.B.1.4	Site Decontamination		100%

ADP CR3 Decommissioning Quarterly Report
3Q-2023

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
	Remove Plant Systems Intermediate Building		Complete
4.B.1.5	Site Decontamination Remove Plant Systems Turbine Building		100% Complete
4.B.2.1-3	Decontaminate Reactor Building	6/30/2024	83% Complete
4.B.2.4	Decontaminate Auxilliary Building	3/31/2024	20% Complete
4.B.2.5	Decontaminate Intermediate Building	12/20/2023	70% Complete
4.B.4	Site Decontamination Decontaminate Buildings License Termination Planning		100% Complete
4.B.5.1	Site Decontamination Decontaminate Buildings West Settling Pond Remediation		100% Complete
4.B.5.3	Site Decontamination Decontaminate Buildings Transfer Canal Sand Removal		100% Complete
5.1.1	Site Restoration Demolish Turbine Building	12/15/2023	20% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Emergency Feed Water Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Diesel Generator Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Alternate AC Diesel Generator Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Fire Pump House Building		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures RB Maintenance Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures RX Vessel Closure Head Storage Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures Hot and Cold Shopt Bldg Demo		100% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures PAB Building Demo	02/06/2024	0% Complete
5.1.2	Site Restoration Demolish Miscellaneous Site Structures	12/06/2023	0% Complete

ADP CR3 Decommissioning Quarterly Report
3Q-2023

	PAY ITEM/MILESTONE	PLANNED COMPLETE	STATUS
	BWST Building Demo		
5.1.2	Site Restoration Demolish Miscellaneous Site Structures NAB Building Demo	6/11/2024	0% Complete
5.1.3	Site Restoration Demolish Miscellaneous Site Structures Auxilliary Building Demo	6/30/2024	0% Complete
5.1.5	Site Restoration Demolish Miscellaneous Site Structures Intermediate Building Demo	6/1/2024	0% Complete
5.2.1	Site Restoration Firing Range Closure		100% Complete

Notes:

Progress Photos

Large Component Removal Work

Reactor Vessel Segmentation

Installation of Heavy Lifting and Rigging System in the Reactor Building




Completed Top RV Section Segmentation and Packaging



Middle RV Section Segmentation Removal



Top Package in Storage, Final Insulation Removal, Completed RV Bottom Horizontal Pre-Cut

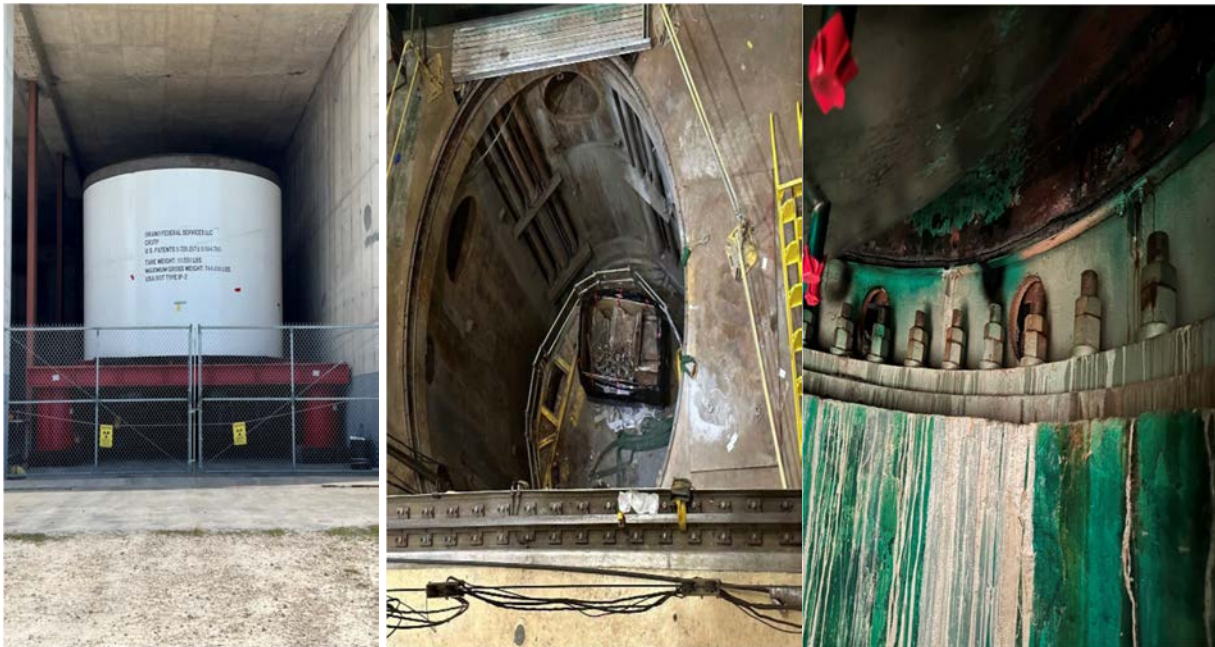


Asbestos Abatement

Turbine Building




Auxilliary Building Plant System Removal and Decon


Elev 162

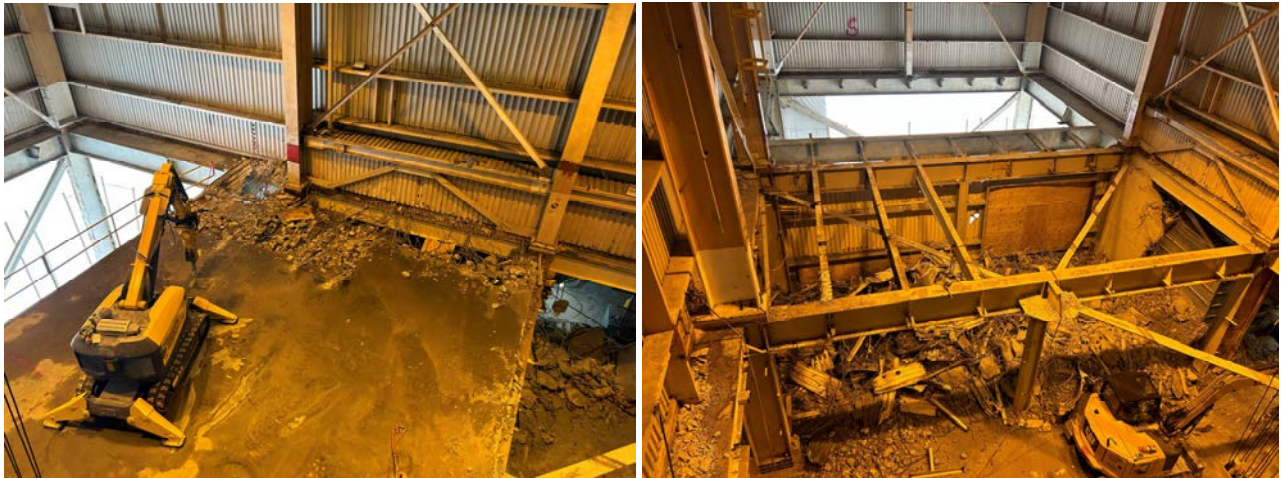

Elev 143

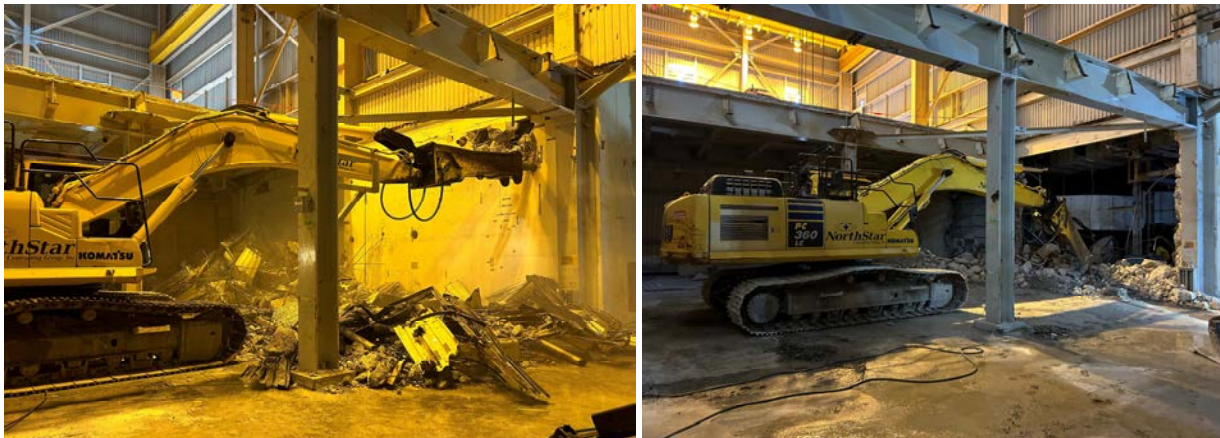

Loadout of Material from Aux Building

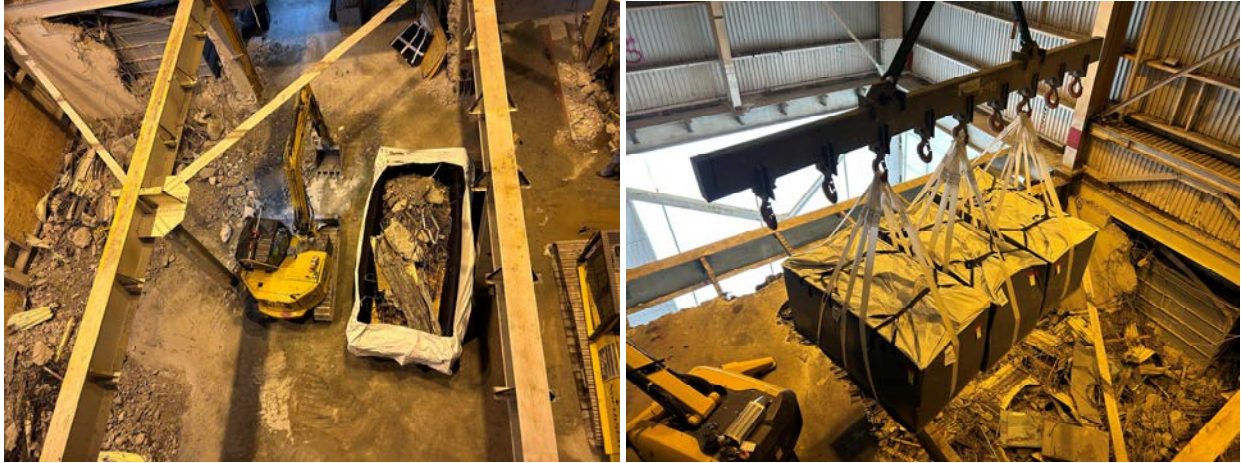

Intermediate Building Decontamination




Turbine Building Demolition





Hot and Cold Shop Demolition

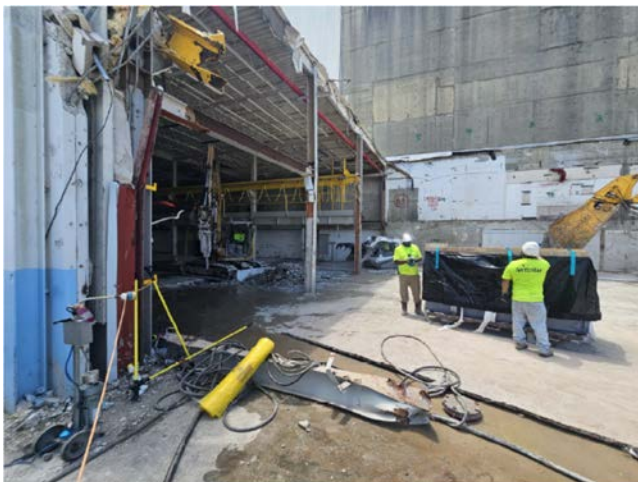

Activity ID	Activity Name	Orig Dur	Rem Dur	% Comp	Start	Finish	2024				2025				2026											
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4							
Crystal River #3 Decommissioning BL September 30, 2023 Schedule Update							1606	848		10-Aug-20 A	31-Dec-26															
A2800	Complete Milestone #1 Partial License Termination	0	0	0%		31-Dec-26*																				
3 - Planning / Site Preparation							138	138		02-Oct-23	10-Apr-24															
D&D Planning & Preparations							138	138		02-Oct-23	10-Apr-24															
LCR & RV/RVI Planning & Engineering							9	9		02-Oct-23	12-Oct-23															
RV Planning, Engineering, & Procurement							9	9		02-Oct-23	12-Oct-23															
Balance of Plant D&D Planning							138	138		02-Oct-23	10-Apr-24															
Demolition Planning							138	138		02-Oct-23	10-Apr-24															
4 - Decommissioning							1342	584		06-Oct-20 A	25-Dec-25															
4A - Large Component Removal							959	201		06-Oct-20 A	08-Jul-24															
Reactor Internals Segmentation							125	125		02-Oct-23	22-Mar-24															
Reactor Internals Waste Packaging, Transportation & Disposal							125	125		02-Oct-23	22-Mar-24															
Reactor Vessel Segmentation							142	125		11-Aug-23 A	22-Mar-24															
Reactor Vessel Segmentation							47	15		07-Sep-23 A	20-Oct-23															
Reactor Vessel Waste Packaging, Transportation & Disposal							125	125		11-Aug-23 A	22-Mar-24															
Large Component Removal Additional Cost							959	201		06-Oct-20 A	08-Jul-24															
Asbestos Abatement							887	129		06-Oct-20 A	28-Mar-24															
Remedial Action Surveys							606	18		30-Jun-21 A	25-Oct-23															
Remove Contaminated Outdoor Piping							200	200		03-Oct-23	08-Jul-24															
4B - Site Decontamination							932	520		19-Aug-21 A	26-Sep-25															
Remove Plant Systems							743	175		08-Sep-21 A	31-May-24															
Reactor Building							180	175		16-Jan-23 A	31-May-24															
Auxiliary Building (95' Elev.)							140	24		08-Sep-21 A	02-Nov-23															
Auxiliary Building (119' Elev. and Above)							80	15		11-Oct-21 A	20-Oct-23															
Remove Plant Systems Waste P,T,&D							400	160		03-Jan-22 A	31-May-24															
Decontaminate Buildings							371	324		03-Jul-23 A	26-Dec-24															
Reactor Building (95' Elev.)							140	140		02-Oct-23	12-Apr-24															
Reactor Building (119' Elev.)							240	240		02-Oct-23	30-Aug-24															
Reactor Building (160' Elev. and Above)							324	324		02-Oct-23	26-Dec-24															
Auxiliary Building							339	80		27-Jul-23 A	23-Apr-24															
Intermediate Building							120	36		03-Jul-23 A	20-Nov-23															
Miscellaneous Site Structures							100	100		08-Dec-23	25-Apr-24															
Decontaminate Buildings Waste P,T & D							575	520		02-Jan-23 A	26-Sep-25															
Reactor Building Waste P,T,&D							360	360		30-Oct-23	14-Mar-25															
Auxiliary, Intermediate, and Misc Building Waste P,T,&D							520	520		02-Jan-23 A	26-Sep-25															
License Termination Planning							5	5		02-Oct-23	06-Oct-23															
Decon Additional Costs							873	321		19-Aug-21 A	23-Dec-24															
Underground Services Excavation							120	120		09-Jul-24	23-Dec-24															
Remedial Action Surveys							630	78		19-Aug-21 A	17-Jan-24															
Tooling and Equipment							40	40		11-Apr-24	05-Jun-24															
Lead Abatement							80	80		02-Oct-23	19-Jan-24															
4F - License Termination							260	260		27-Dec-24	25-Dec-25															
License Termination Planning, Final Surveys, Reporting							260	260		27-Dec-24	25-Dec-25															
License Termination							140	140		27-Dec-24	10-Jul-25															
Confirmation & Verification Surveys							110	110		02-May-25	02-Oct-25															
Terminate License							60	60		03-Oct-25	25-Dec-25															
5 - Site Restoration							913	848		10-Aug-20 A	30-Dec-26															
Demolition, Backfill, Grading							913	848		10-Aug-20 A	30-Dec-26															
Turbine Building							130	60		03-Jul-23 A	22-Dec-23															
Miscellaneous Site Structures							250	135		10-Aug-20 A	31-Oct-24															
Auxiliary Building							80	53		23-Jan-23 A	05-Jul-24															
Reactor Building							524	524		27-Dec-24	30-Dec-26															
Intermediate Building							45	45		09-Jan-23 A	21-Feb-24															

█ Remaining Level of Effort
 █ Actual Work
 █ Critical Remaining Work
▬ Primary Baseline
 █ Remaining Work
 ◆ Milestone

Activity ID	Activity Name	Orig Dur	Rem Dur	% Comp	Start	Finish	2024				2025				2026			
							Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
	Backfill and Grade	534	534		25-Dec-23	08-Jan-26												08-Jan-26, Backfill and Grade
	Site Restoration Additional Costs	364	364		22-Feb-24	15-Jul-25												15-Jul-25, Site Restoration Additional Costs
	Concrete Crushing & Security Barriers	364	364		22-Feb-24	15-Jul-25												15-Jul-25, Concrete Crushing & Security Barriers
	Concrete Crushing	345	345		22-Feb-24	18-Jun-25												18-Jun-25, Concrete Crushing
	Security VBS	19	19		19-Jun-25	15-Jul-25												15-Jul-25, Security VBS

